## Enclosure 5. Photograph index

49 photographs of the floor at the property, taken by the family.

August 19, 2026 (4): the day the work ended.

September 2, 2026 (6): close-ups of the surface and joints.

September 21, 2026 (1): the installed red oak beside the original white oak.

September 22, 2026 (38): walkthrough of the great room and office.

Each photograph carries its capture date in the file name. Original files with metadata are available on request.

Index: date, number, and what the photograph shows.



**2026-08-19 photo 01**
unsanded mill marks, no expansion gap at wall



**2026-08-19 photo 02**
grain mismatch, sanding swirls



**2026-08-19  photo 03**
mill marks, board color mismatch



**2026-08-19  photo 04**
no expansion gap at wall, grain mismatch



**2026-09-02 photo 01**
cross grain sanding scratches



**2026-09-02 photo 02**
unsanded mill marks on board



**2026-09-02 photo 03**
putty filled joint, uneven edge



**2026-09-02 photo 04**
wood filler at butt joint, color mismatch



**2026-09-02 photo 05**
mill marks, end gap short board



**2026-09-02 photo 06**
mill marks cathedral chatter, unsanded




## 2026-09-21 photo 01

SPECIES COMPARISON, red oak installed vs white oak original



## 2026-09-22 photo 01

baseboard horizontal, no gap, end joint slip



**2026-09-22 photo 02**
baseboard horizontal, no gap



**2026-09-22 photo 03**
baseboard horizontal, no gap



**2026-09-22 photo 04**
baseboard horizontal, no gap



**2026-09-22 photo 05**
baseboard horizontal, floor cut under baseboard



**2026-09-22 photo 06**

quarter round hiding gap, door jamb, vertical grain



**2026-09-22 photo 07**

stain mark, mill marks, end joint slip



**2026-09-22 photo 08**
mill marks unsanded, closeup



**2026-09-22 photo 09**
mill marks unsanded, raking light



**2026-09-22 photo 10**
slippage, raised end joint, low angle



**2026-09-22 photo 11**
burn stain mark, grain mismatch



**2026-09-22 photo 12**
overall, dining room, raking light mill marks



**2026-09-22 photo 13**
overall, dining room, raking light



**2026-09-22 photo 14**
split gap at joint




**2026-09-22 photo 15**
baseboard vertical, board end tight to jamb, no gap



**2026-09-22 photo 16**

baseboard horizontal, wall run, no gap

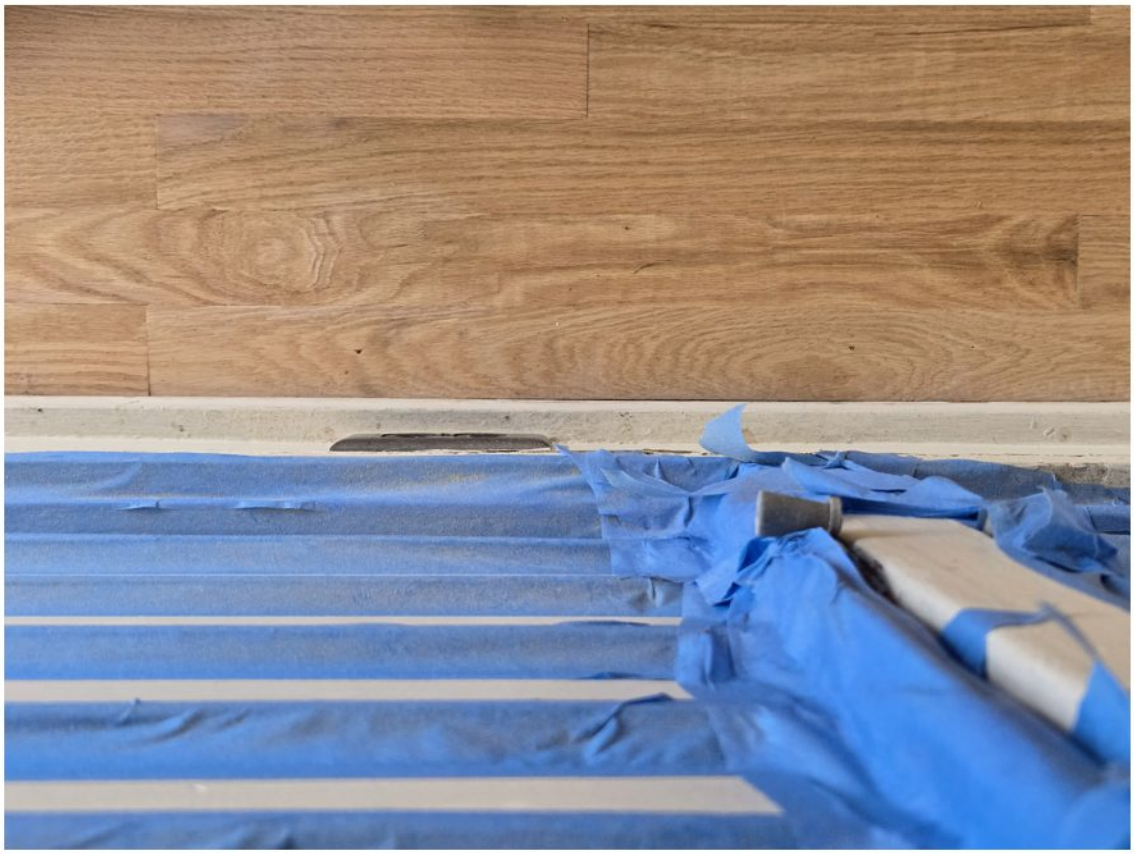

**2026-09-22 photo 17**

baseboard horizontal, taped, no gap



**2026-09-22 photo 18**
quarter round staged to hide gap



**2026-09-22 photo 19**
overall, floor and baseboard, chair



**2026-09-22 photo 20**
mill marks unsanded, board



**2026-09-22 photo 21**
slippage, open end joint, grain mismatch



**2026-09-22 photo 22**
slippage, open end joint, grain mismatch




**2026-09-22 photo 23**
slippage, open butt joint, grain mismatch



**2026-09-22 photo 24**
baseboard left in place, wall



**2026-09-22 photo 25**
face nail exposed, no gap at jamb

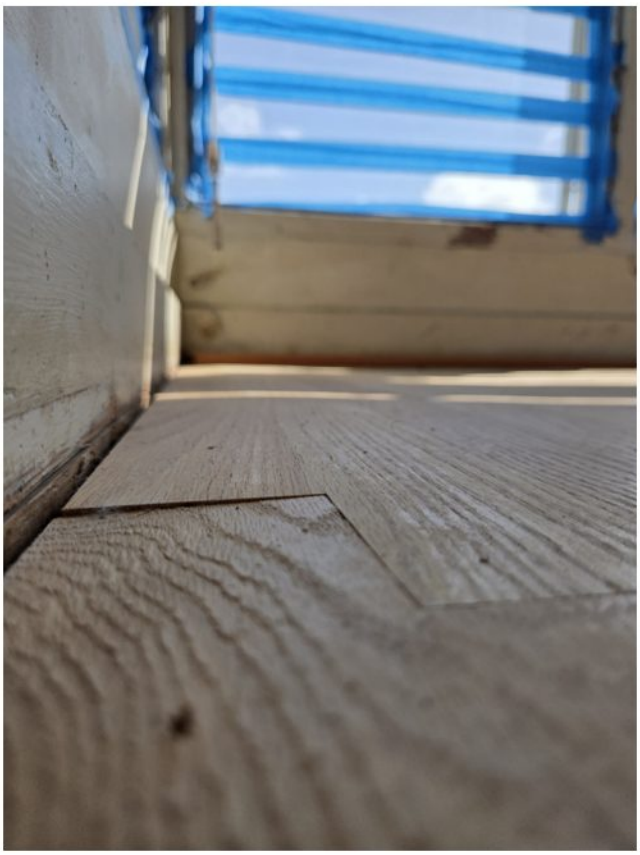

## 2026-09-22 photo 26

baseboard vertical, board ends at window wall, no gap



## 2026-09-22 photo 27

slippage, open joint, chipped edge



**2026-09-22 photo 28**
slider threshold, no reducer, subfloor exposed



**2026-09-22 photo 29**
slider threshold, raw edge, subfloor exposed



**2026-09-22 photo 30**
tile transition, no threshold, raw edge



**2026-09-22 photo 31**
baseboard horizontal, no gap



**2026-09-22 photo 32**
baseboard horizontal, no gap



**2026-09-22 photo 33**
tile transition, baseboard in place, no reducer



**2026-09-22 photo 34**

OVERALL, living room, ocean view



**2026-09-22 photo 35**

OVERALL, living room, wide




**2026-09-22 photo 36**

OVERALL, living room, wide 2



**2026-09-22 photo 37**

mill marks unsanded, best closeup

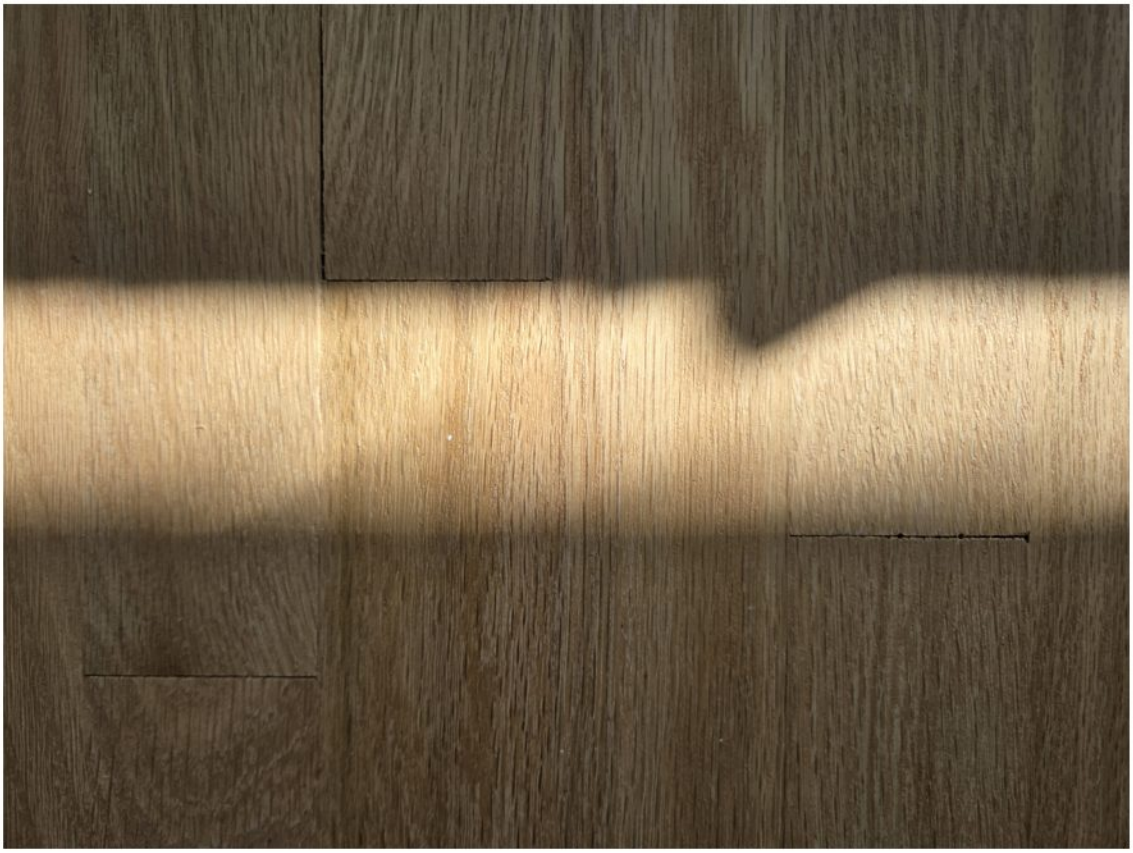

**2026-09-22  photo 38**

sun stripe, end joint gaps, grain mismatch
